2021 International Horticultural Expo Preparatory Report

Yangzhou People’ s Government

After 2016，with the help and support of AIPH we progressively advance preparatory work in all respects.

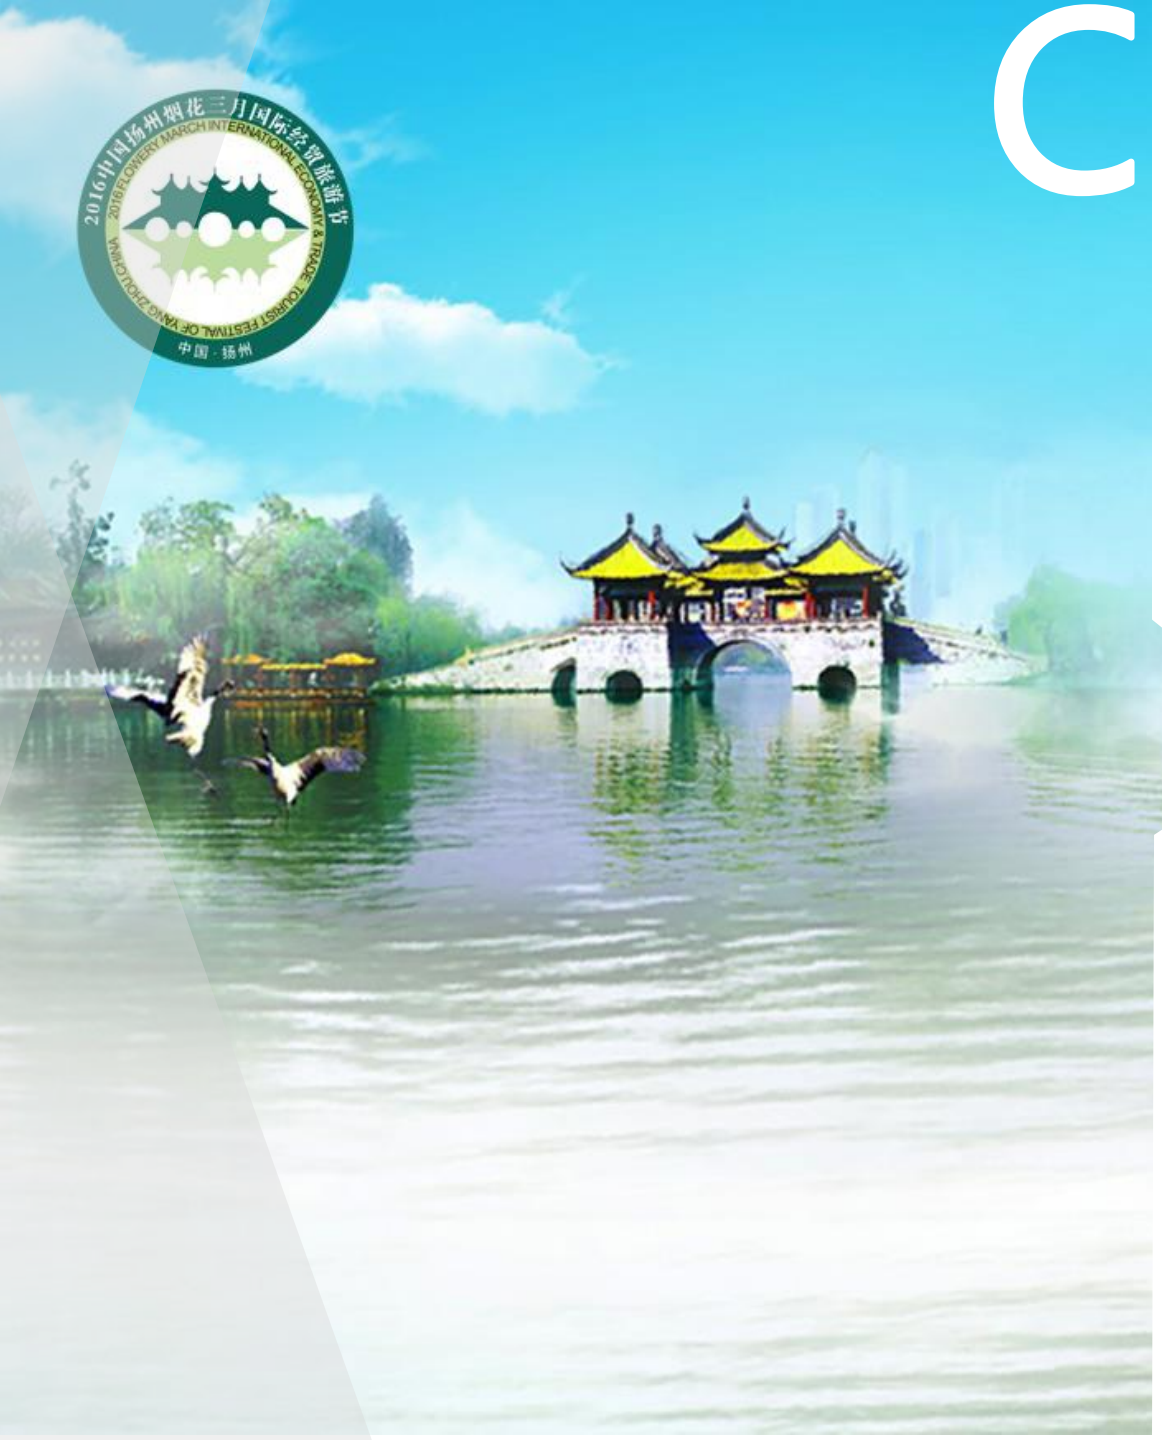

Contents

1. preparatory organization
2. planning
3. transport network
4. landscape and greening
5. supporting services
6. Platform for Action
7. investments & international participation

I. We started to form the preparatory working organization

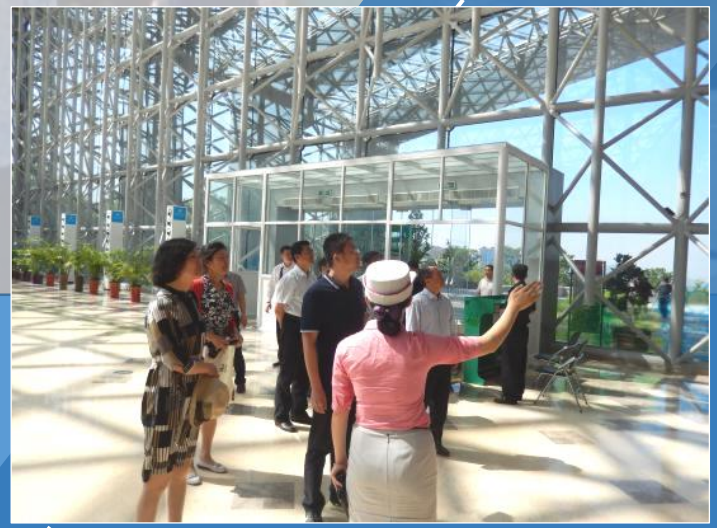

·inspection trips to Qingdao, Tangshan,
·study preparatory organization structure, marketing programs, developmental modes, funding, construction management and post-Expo operation
·send staff to Beijing World Horticultural Expo Coordination Bureau

· one of 10 major projects of Yangzhou in the next 5 years.
· on Yangzhou level: Preparing Committee of 2021 Yangzhou Expo, in charge of strategic implementation;

· Yizheng level: construction headquarter, responsible for planning and construction.
· approval procedure of holding Yangzhou Expo.
· later: Executive Committee of Yangzhou Expo & Organizing Committee from the national and provincial level.

Construction Headquarter

Approval Procedure

Coordination & progress

II. We solidly make our efforts on planning.

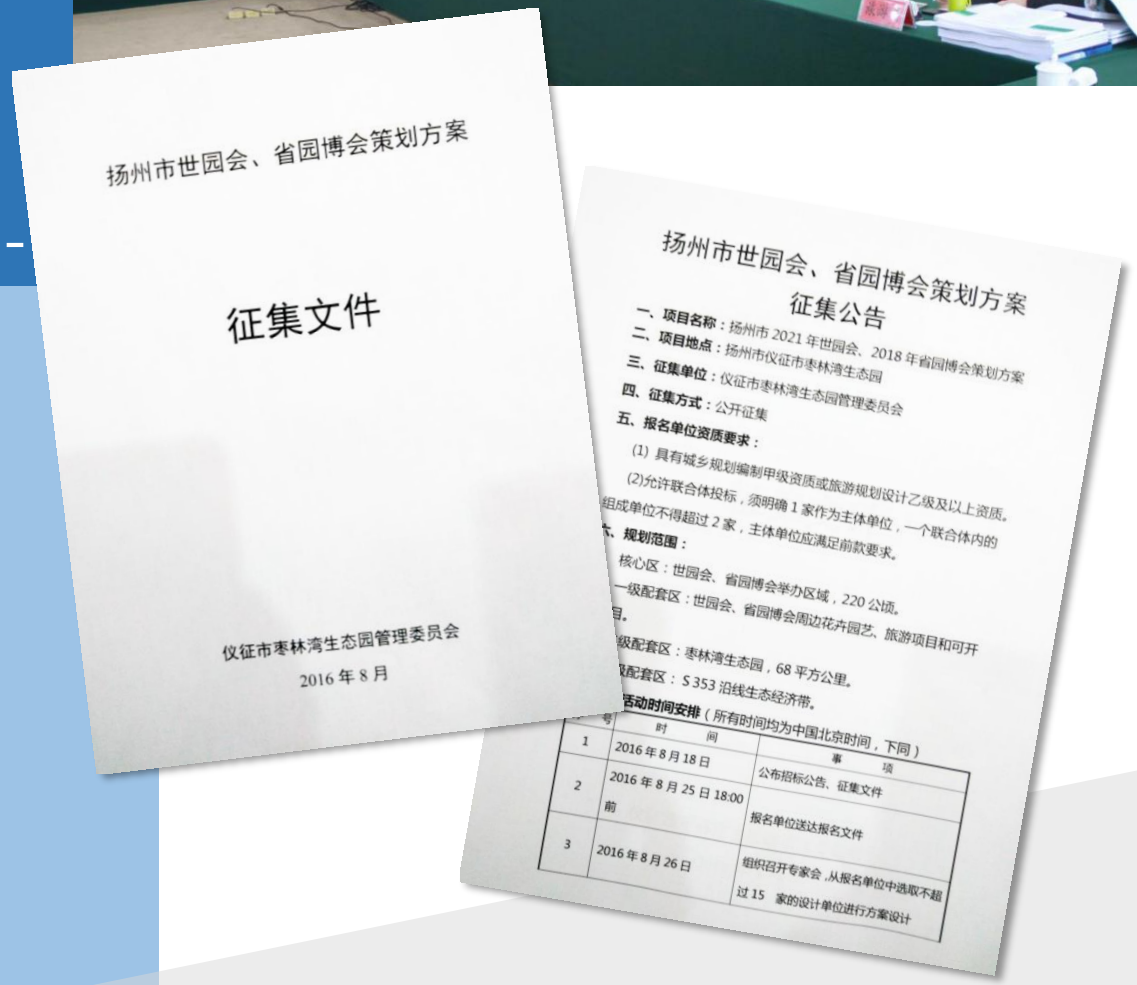

· announced tender notice

· invite THUPDi from Tsinghua University to study and integrate these plans,

· **6 principles**: keeping pace with the times, setting green as foundation, coordinated development, low carbon and environmental protection, interaction and participation, and sustainability.

Total planned surface: 320 ha

eastern part: 200 ha - international pavilions and gardens and other Chinese cities’ gardens.

western part:120 ha - Jiangsu pavilions and gardens

N
01
02
03
04
05
06
07
08
09
10
11
12
13
14
15
16
17
18
19
20
21
22
23
24
22

·10th Jiangsu Horticultural Exposition : **September 2018.**

· main pavilion, folk art village, craft of gardens: completed in July, 2018.

· Jiangsu Expo will be adjusted into Jiangsu section in 2021

specialized infrastructure plans:
surrounding roads,
municipal engineering,
water conservancy, etc.

规划设计

1	研究工作			
1.1	开展园区客流预测专项调研	2016年10月	2016年12月	规划设计组
1.2	完成策划方案编制	2016年10月	2016年12月	规划设计组
2	总体规划			
2.1	完成省园博会举办方案向省厅报批	2016年11月	2016年11月	规划设计组
2.2	确定省园博会修建性详细规划编制单位	2016年10月	2016年11月	规划设计组
2.3	编制完成省园博会修建性详细规划方案	2016年11月	2017年1月	规划设计组
3	专项规划			
3.1	完成两园项目区和重点区域测绘工作	2016年10月	2017年2月	规划设计组
3.2	编制完成枣林湾全域绿化美化方案	2016年10月	2016年11月	工程建设组
3.3	编制完成枣林湾综合交通规划	2016年10月	2016年12月	规划设计组
3.4	完成枣林湾道路绿化施工图设计	2016年11月	2016年12月	工程建设组
3.5	完成土方工程施工图设计	2017年1月	2017年1月	规划设计组
3.6	编制完成建筑单体、景观、市政、运营服务设施、总体种植规划等单项设计	2017年1月	2017年5月	规划设计组
3.7	组织城市展园设计	2017年3月	2017年6月	规划设计组
3.8	编制安置区方案	2016年11月	2016年12月	规划设计组
3.9	属于世园会但目前需与省园博会同步启动的相关规划	2016年12月	2018年10月	规划设计组
4	技术规程			
4.1	编制室内布展技术规程	2017年1月	2017年4月	规划设计组
4.2	编制室外布展技术规程	2017年1月	2017年4月	规划设计组
4.3	指导园林园艺技术活动	2018年9月	2018年10月	规划设计组

III. we improve transport network.

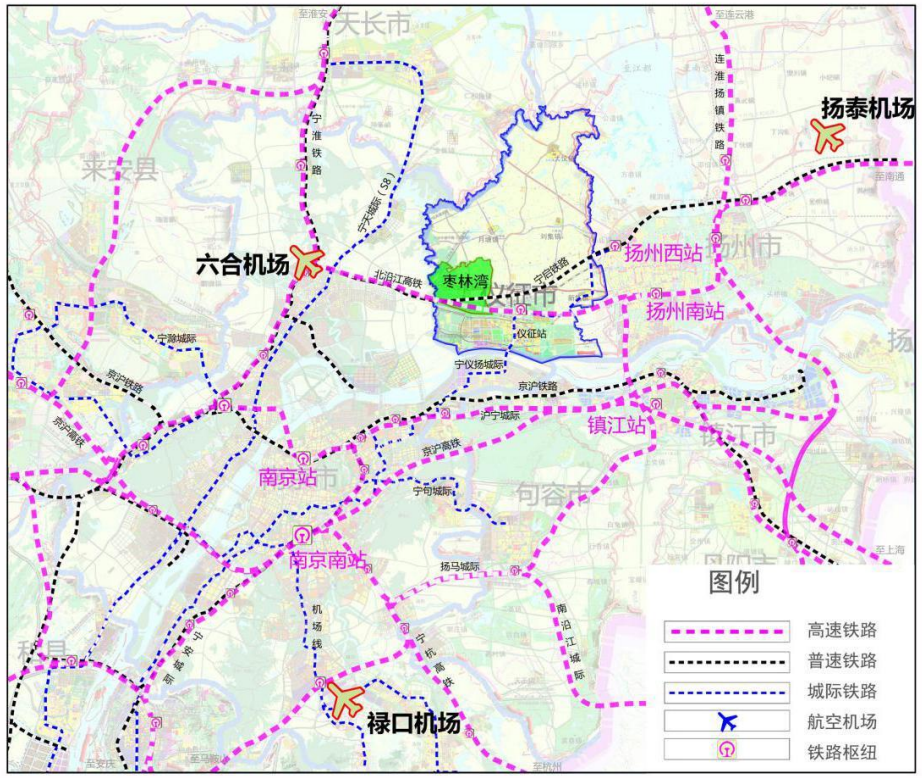

·2 highway exits added: 1.5 km north; 3 km south.
· Approved by Jiangsu Provincial Government
· Construction under progress and will be finished to operate in this August.

南京
扬州

G328汉金大道互通效果图
中设设计集团股份有限公司

G328 节点效果图

G328 绿化方案

National Road 328 (Nanjing to Yangzhou)
Provincial Road 439 (Nanjing to Yizheng).
Yizheng Highspeed Railway Station, 3 km east of the expo site, is under progress of renovation
Integrated transportation hub launched.

IV We improve public landscape and greening.

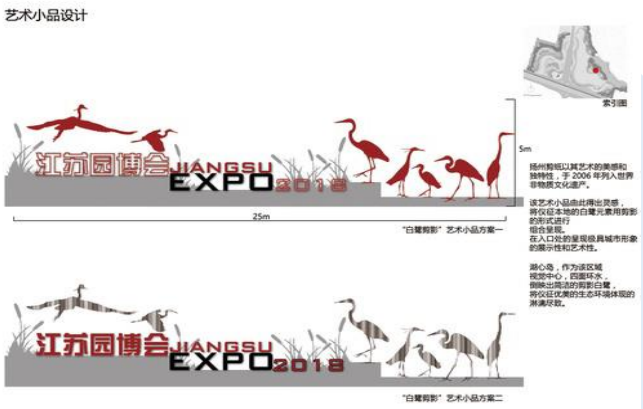

Taking the opportunity of holding Jiangsu Horticultural Expo this year, Yangzhou significantly strengthen greening and afforestation by starting up upgrading projects of peripheral landscaping and greening.

Hanjin Road: formed trees, ground covers and rockery arrangement basically completed;
Zaolin Road: terrain rearrangement, nursery planting under progress & pipeline laying
Tianchi Road: greening plan finished

Surrounding the expo site, 720,000 cubic meters of earthwork have been done, plus newly planted 10,000 nurseries, 24,000 m2 shrubs and 240,000 lawns.

V. We enhance tourist supporting services.

Facility Capacity & Tourist Population

	Total Tourists (million people)	Number of beds		Dining Seats (Pax)	
2020	3	6580		10000	
2030	4	11100		14000	
2018 during Jiangsu Expo	1.3	Daily Average	Peak day	Daily Average	Peak day
		11200	16800	12600	18900
2021 during the Expo	7.2	Daily Average	Peak day	Daily Average	Peak day
		10400	15735	11700	17700

To meet the demand of receiving visitors during the expo, we investigated facilities like hotels, restaurants, hospitals, etc. within 1-hour transport circle and speculate the estimate number of visitors, according to which we started an upgrading program for accommodations.

tentative plan of hotel accommodation distribution

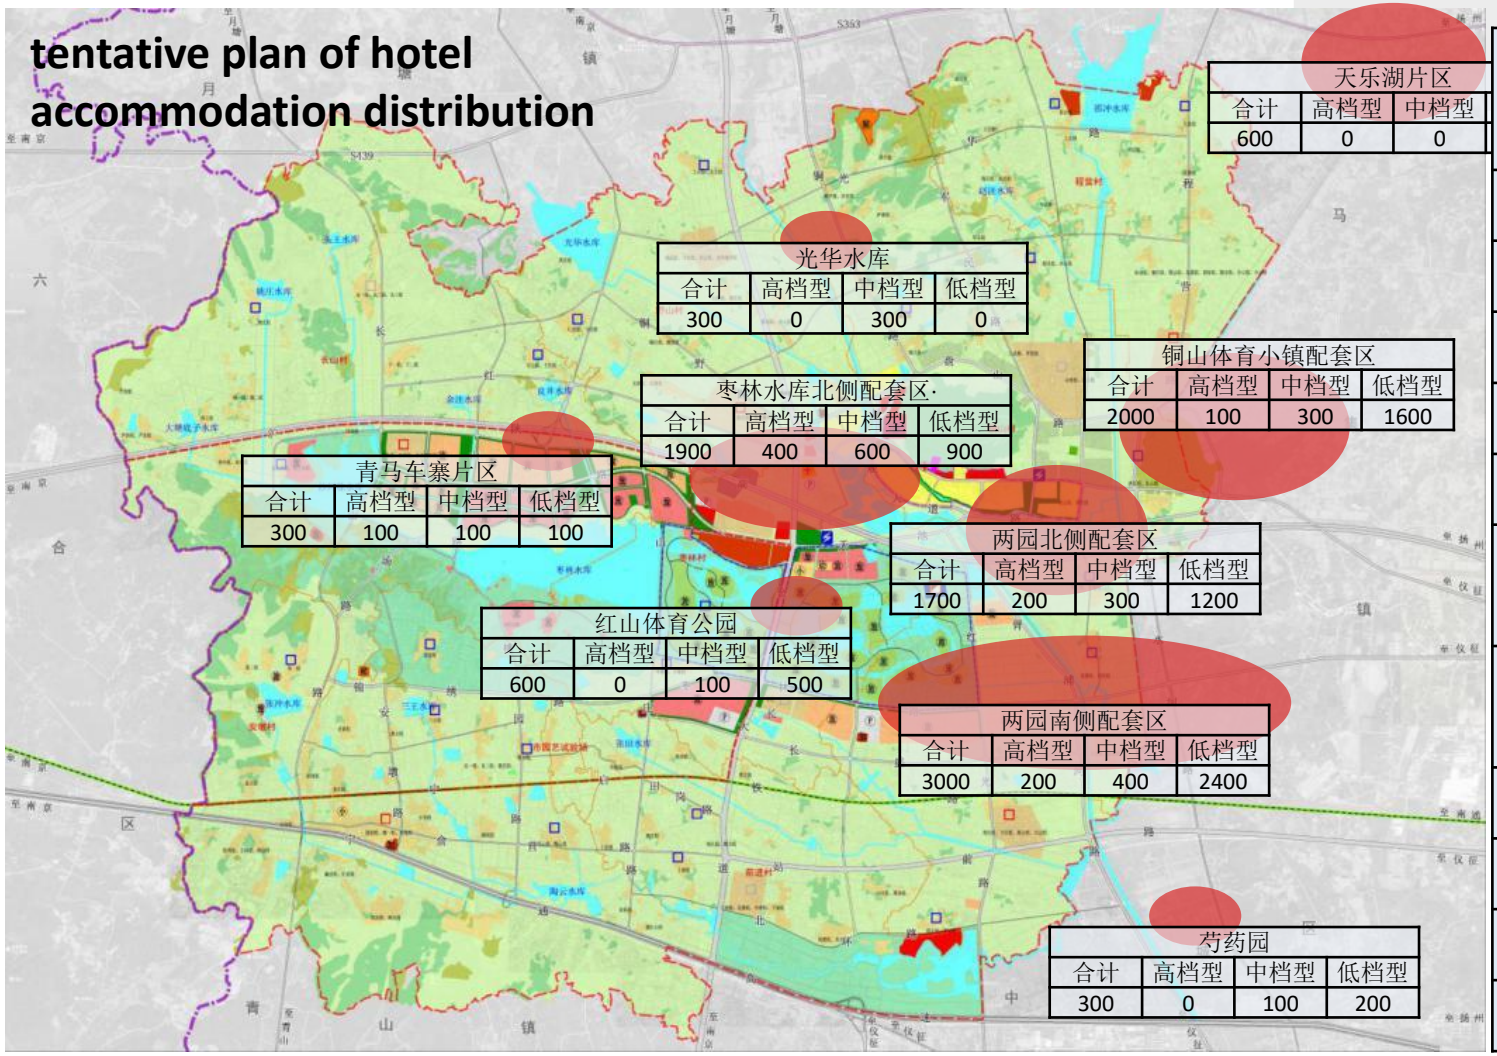

片区	床位数（床）			
	合计	高档型	中档型	低档型
天乐湖片区	600	0	0	600
光华水库	300	0	300	0
青马车寨片区	300	100	100	100
芍药园	300	0	100	200
红山体育公园	600	0	100	500
铜山体育小镇配套区	2000	100	300	1600
枣林水库北侧配套区	1900	400	600	900
两园北侧配套区	1700	200	300	1200
两园南侧配套区	3000	200	400	2400
其他村庄民宿	400	50	50	300
总计	11100	1050	2250	7800

This program consists of a set of commercial facilities, an Expo Village north of the site, a characteristic town as supporting service area 1 km away from the site, which will provide with all-around supporting services.

VI. We make the Platform for Action.

· Preliminary **Platform for Action** of International Horticultural Exposition 2021 Yangzhou in initial stage

· Set the timetable and key tasks of every stage of preparation

After certain procedure been finalized, we will make rounds of amendments with the Platform for Action following the requirements of AIPH and CFA.。

VII We make plans beforehand on inviting investments and international participation

We have already talked some of garden constructors and event operators in China and had cooperation intentions. Currently we put this job in a key part in all foreign affairs in Yangzhou; we have contacted and visited some of the cities in southeastern Asia and World Canal Cities Organization concerning this issue.

Next, continue to facilitate relative procedures in China, to plan and construct Yangzhou Expo with high standard, to thoroughly improve regional environment and facilities, to efficiently attract business partners and exhibitors, for the purpose of hosting a horticultural gala with Yangzhou characteristics and international level.

東關街
THANKS
i caffè
